

AMI Update

Board of Water Commissioners - August 6, 2020




COVID-19

- Project was temporarily suspended
 - March 20 – May 15
 - New end date: Feb. 28, 2021
- Tribus staff being affected
 - Minimizing in-person interaction between LBWD staff and Tribus staff



Meter Installation Progress

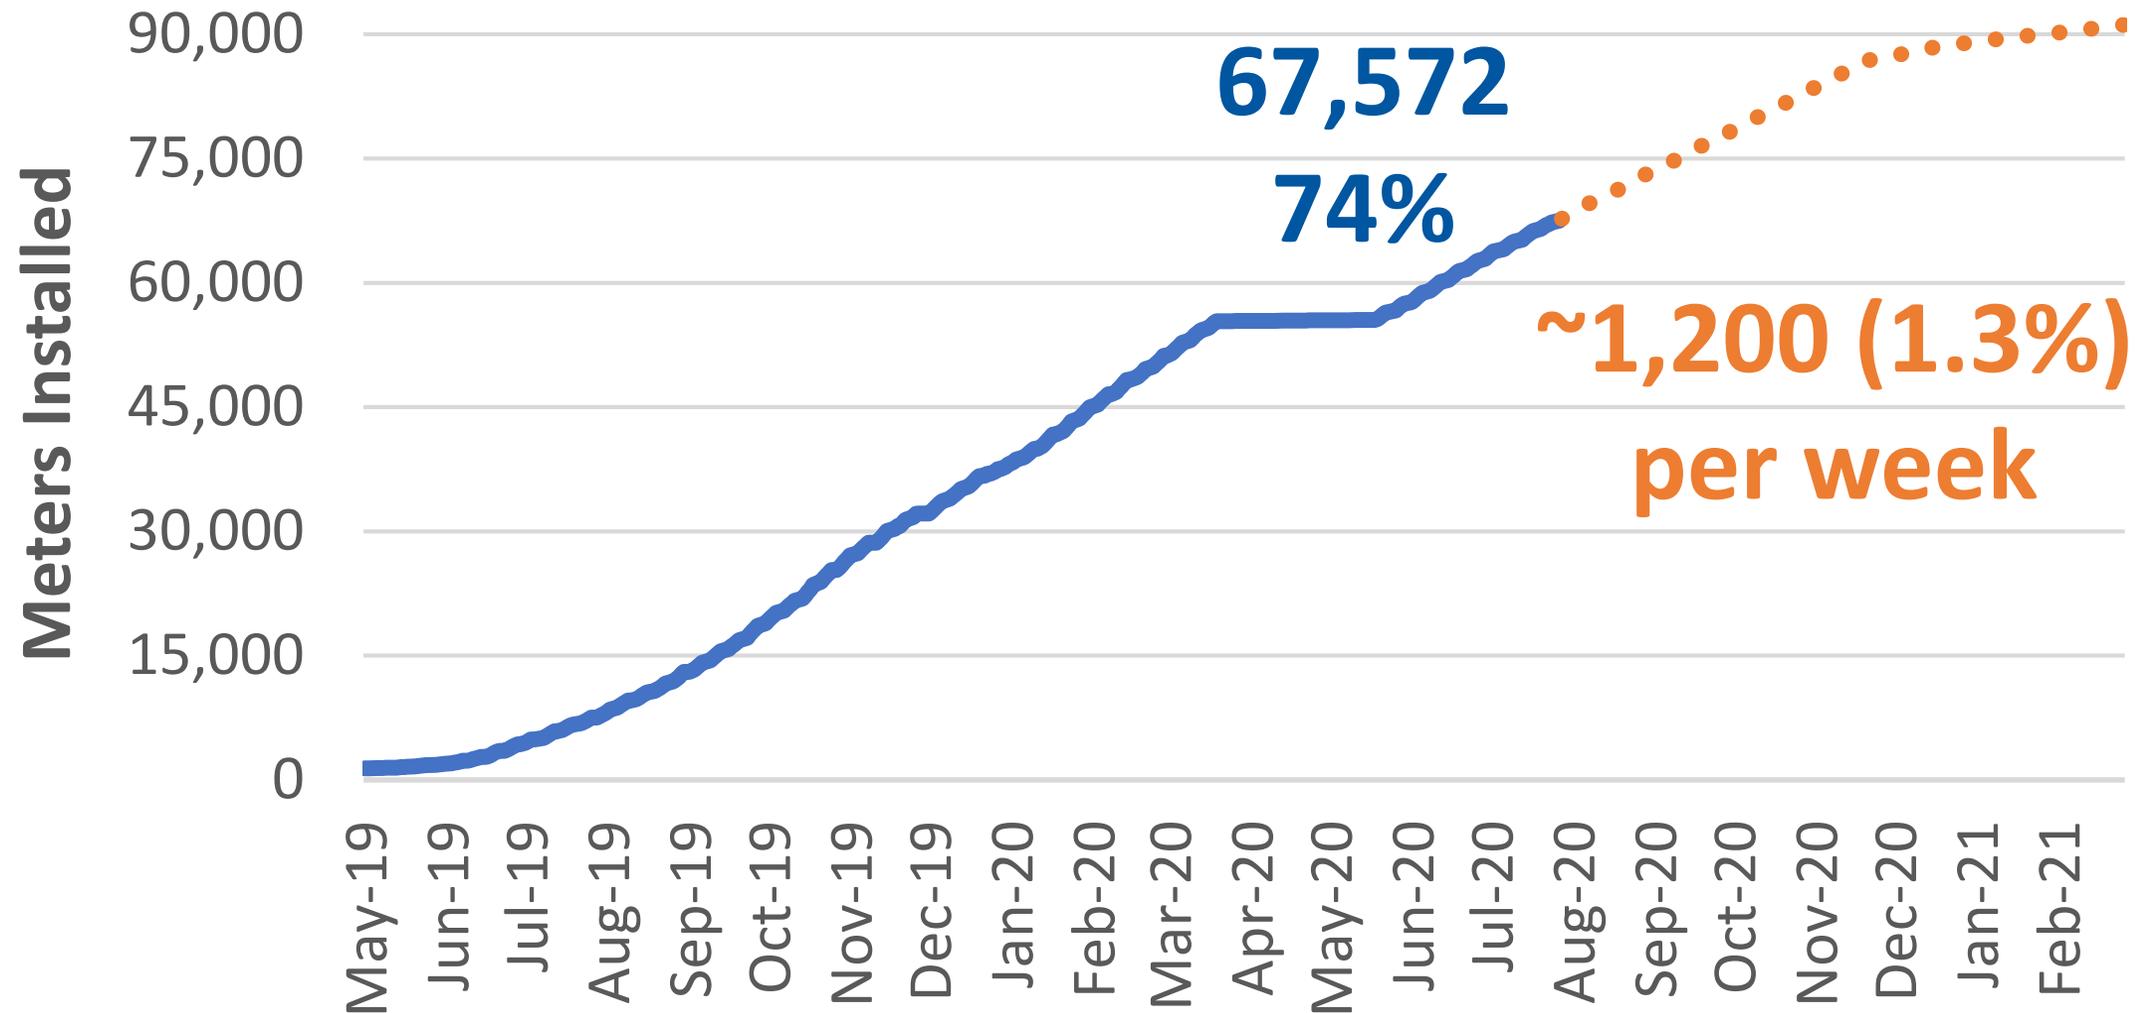

Project Costs

	Contract Value (millions)	Expended (millions)
Parts	\$20.0	\$18.3
Installation	\$4.9	\$2.3
Project Management	\$1.2	\$1.1
Total	\$26.1	\$21.7



Project Lease Financing

Lease Principal Amount	\$27.4
------------------------	--------

Contract Values	\$26.1
-----------------	--------

Contingency Remaining	\$1.3
------------------------------	--------------

Costs Reimbursed to Date	\$20.3
--------------------------	--------



Questions?



Long Beach Water

Exceptional Water • Exceptional Service
