ALAMITOS BAY MARINA RESTROOM IMPROVEMENTS PROJECT




MARINE ADVISORY COMMISSION MEETING

09/08/2022







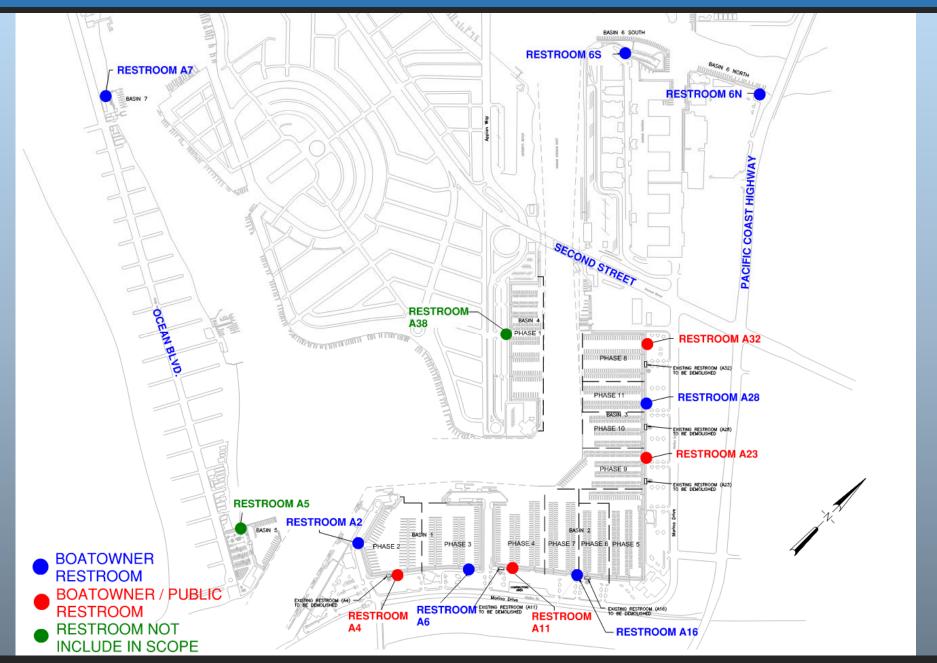

ALAMITOS BAY MARINA, CA – OVERALL RESTROOMS LAYOUT





Regulatory Permitting

- 1) Submitted Permit Conformance Request to Regulatory Agencies
 - ✓ California Coastal Commission Coastal Development Permit (CDP)

Local Building Permitting

- 2) Completed Initial Coordination with Building Department
 - ✓ June 2021 Initial Review and Comment Received (P. Yin)


Conceptual Design

- 3) Recommended Layout & Building Alternatives
 - ✓ June 2022 Marine Bureau Review and Coordination
- 4) Completed Geotechnical Site Investigation
 - Seismic Liquefaction Considered Per Most Recent Building Codes
 - Shallow Foundations Allowed Per Geotechnical Finding

EFFORTS COMPLETED TO-DATE






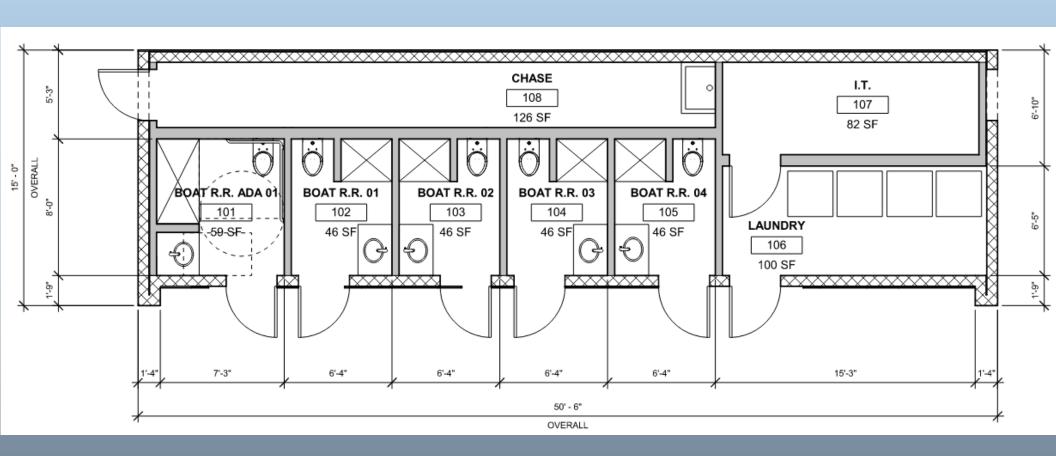

CONCEPTUAL BUILDING LAYOUT – BOATOWNER RESTROOM



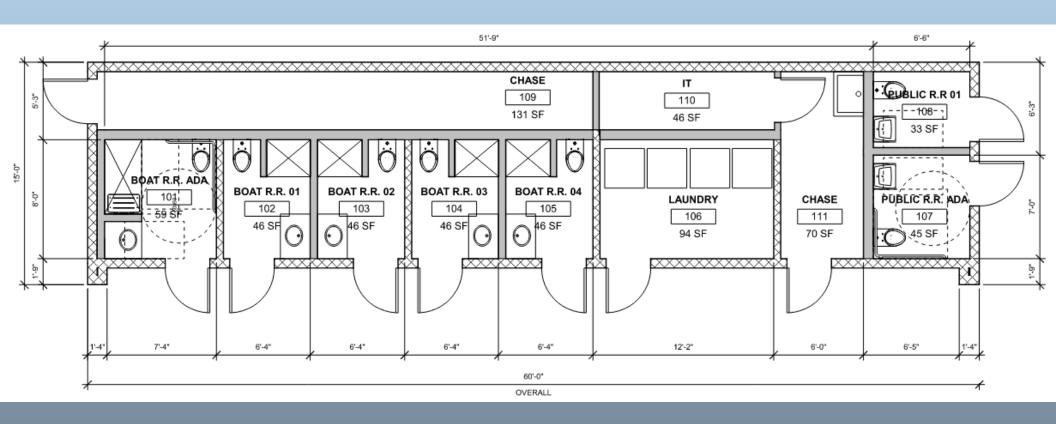

CONCEPTUAL BUILDING LAYOUT - BOATOWNER / PUBLIC RESTROOM





CONCEPTUAL RESTROOM BUILDING EXTERIOR RENDERING





- 1) Marine Advisory Commission Coordination
 - △ Commission Design Review September 8, 2022
- 2) Final Design Phase

3) Long Beach Development Services Local Building Permit

- 4) Bid Advertisement & Construction
 - ✓ Phase 1 Restrooms A4 and A23

Final Design Phase
Oct 2022 – Mar
2023

City Plan Check
Mar – Apr
2023

Bid & Award May — Jun 2023 Construction
Jul 2023 – Apr
2024

ESTIMATED PROJECT SCHEDULE



THANK YOU! ALAMITOS BAY MARINA RESTROOM IMPROVEMENTS PROJECT

For more information, please contact:

Jerry Holcomb, P.E.
Moffatt & Nichol
Waterfront Project Engineer
JHolcomb@moffattnichol.com

