14-0057

Long Beach Schedule 2013-14 REVISED.mpp

ID	Contract Task	Task Name	Duration	Start	Finish	Predecessors	Resource Names
0	0	**2013/14 Long Beach PMP Update**	**359.38 days**	**Fri 8/16/13**	**Tue 9/30/14**		
1	0	Project Initiation	109.25 days	Fri 8/16/13	Wed 12/18/13		
2	0						
3	0	Partial Award/Scope Confirmation	0 days	Fri 8/16/13	Fri 8/16/13		
4	1	Project Initiation & Set Up	67.38 days	Fri 8/16/13	Thu 10/31/13	3	
5	2	Investigations & Network Definition	60.13 days	Mon 9/9/13	Fri 11/15/13		
6	3	Network Classification	55.63 days	Mon 9/9/13	Fri 11/15/13		
7	0	Full Contract NTP	0 days	Tue 9/17/13	Tue 9/17/13		
8	0	Contract Execution & Purchase Order	0 days	Wed 12/18/13	Wed 12/18/13		
9							
10	0	Surface Distress Survey & Data Processing	117.38 days	Mon 11/25/13	Mon 4/7/14		
11							
12	4	Field Survey Routing and Set up	31 days	Mon 11/18/13	Mon 12/23/13		
13	5	Laser RST Mobilization and Calibration	2 days	Mon 1/6/14	Tue 1/7/14	12	
14	6	Automated Data Collection - District 1	6 days	Wed 1/8/14	Tue 1/14/14	13	
15	7	Automated Data Collection - District 2	6 days	Tue 1/14/14	Tue 1/21/14	14	
16	8	Automated Data Collection - District 3	6 days	Tue 1/21/14	Tue 1/28/14	15	
17	9	Automated Data Collection - District 4	6 days	Tue 1/28/14	Tue 2/4/14	16	
18	10	Automated Data Collection - District 5	6 days	Tue 2/4/14	Tue 2/11/14	17	
19	11	Automated Data Collection - District 6	6 days	Tue 2/11/14	Tue 2/18/14	18	
20	12	Automated Data Collection - District 7	6 days	Tue 2/18/14	Tue 2/25/14	19	
21	13	Automated Data Collection - District 8	6 days	Tue 2/25/14	Mon 3/3/14	20	
22	14	Automated Data Collection - District 9	6 days	Tue 3/4/14	Mon 3/10/14	21	
23	15	Data QA/QC, Processing, and Formatting	24 days	Mon 3/10/14	Mon 4/7/14	22	
24	16	PCI configuration (Life cycle curves)	24 days	Mon 3/10/14	Mon 4/7/14	22	
25	17	Asset Inventory Imagery Acquisition & 2 Year Storage	54.13 days	Wed 1/8/14	Mon 3/10/14	13	
26							
27	0	Subgrade Deflection Survey & Data Processing	62.25 days	Mon 1/27/14	Mon 4/7/14		
28							
29	18	Mobilization and Dynaflect Calibration	6 days	Mon 1/27/14	Sat 2/1/14		
30	19	Arterial Data Collection	26 days	Sat 2/1/14	Tue 3/4/14	29	
31	20	Collector Data Collection	12 days	Tue 3/4/14	Tue 3/18/14	30	
32	21	LBPD Traffic Control	39.88 days	Sat 2/1/14	Tue 3/18/14		
33	22	Data QA/QC, Processing, and Formatting	18 days	Tue 3/18/14	Mon 4/7/14	31	
34							
35	0	Data Management	179.63 days	Mon 3/10/14	Tue 9/30/14		
36							
37	23	Process Forward View Images at 25-foot Intervals - 1 view	24 days	Mon 3/10/14	Mon 4/7/14	22	
38	24	Pavement Data Load to Lucity	12 days	Mon 4/7/14	Mon 4/21/14	23	
39	25	GIS Mapping of Results (Shape, KML, & Geodatabase)	12 days	Mon 4/7/14	Mon 4/21/14	23	
40	26	Strategy Session for Analysis & Reporting	1 day	Mon 4/21/14	Tue 4/22/14	39	
41	27	Analysis Operating Parameter Development	12 days	Tue 4/22/14	Mon 5/5/14	40	
42	28	Draft Maintenance and Budget Analysis Development	18 days	Mon 5/5/14	Mon 5/26/14	41	
43	29	Pavement Analysis Results for Client Review & Input	12 days	Mon 5/26/14	Mon 6/9/14	42	
44	30	Draft Pavement Management Report	18 days	Mon 6/9/14	Sat 6/28/14	43	
45	31	Final Analysis and Report Delivery	12 days	Sat 6/28/14	Sat 7/12/14	44	
46	32	Import of Condition & Analysis Results into MicroPAVER	12 days	Sat 6/28/14	Sat 7/12/14	44	
47	33	Lucity Software, Implementation, & Training	19.38 days	Sat 7/12/14	Mon 8/4/14	45	
48	34	Annual Report Update for 2 Consecutive Years					
49	35	Peer Review Consulting Services	133.75 days	Thu 5/1/14	Tue 9/30/14		
50	36	Pavement Design, Standard Plans, & Specifications Consulting Serv	133.75 days	Thu 5/1/14	Tue 9/30/14		
51	37	Process Planning Consulting	133.75 days	Thu 5/1/14	Tue 9/30/14		
52	38	On Call Supplemental Services (As Needed)	133.75 days	Thu 5/1/14	Tue 9/30/14		
53							
54	0	Traffic Count Services	142.88 days	Mon 11/11/13	Tue 4/22/14		
55							
56	39	Site Selection and Mapping	29.5 days	Mon 11/11/13	Fri 12/13/13		
57	40	48 Hour Counts - Major Arterials	72 days	Mon 1/6/14	Fri 3/28/14		
58	41	48 Hour Counts - Minor Arterials	72 days	Mon 1/6/14	Fri 3/28/14		
59	42	48 Hour Counts - Major Collectors/Industrial/Commercial	72 days	Mon 1/6/14	Fri 3/28/14		
60	43	Classification and Apply Results to GIS	21 days	Fri 3/28/14	Tue 4/22/14	59	

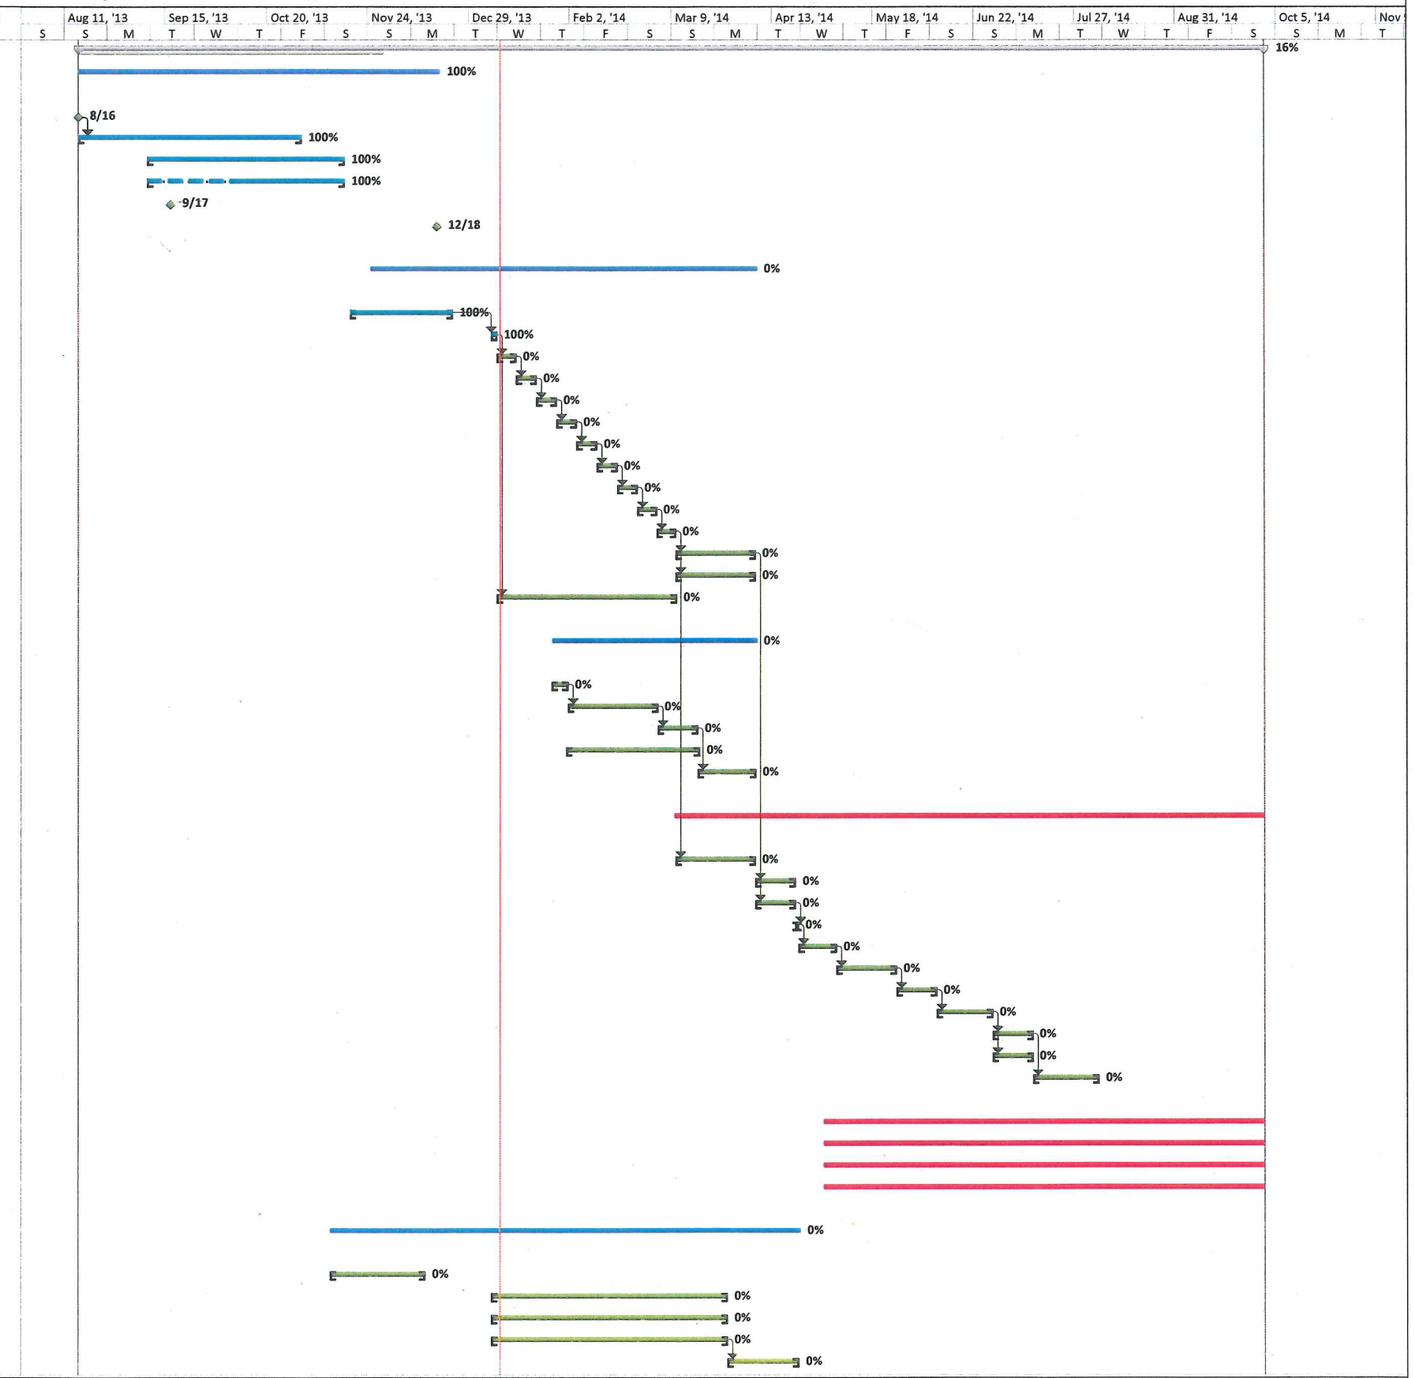

Critical Progress | Task Progress | Finish-only | Critical Split | Baseline Milestone | Summary | External Tasks | Inactive Milestone
Task | Manual Task | Duration-only | Baseline | Milestone | Manual Summary | External Milestone | Inactive Summary
Split | Start-only | Critical | Baseline Split | Summary Progress | Project Summary | Inactive Task | Deadline
